



Start Date: 01JAN07
Finish Date: 11JAN12
Data Date: 05JAN09
Run Date: 29MAY09 14:46

Activity Description	2007												2008												2009
	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN
Delay / Impacts																									
Request for Layout Controls																									
Delayed - Grout Design for Base Plates																									
Majority SOG East of Col Line H																									
Access to Columns NW Corner																									
M&E Impact to Area 3 Columns																									
Incomplete Fdns. @ Line J-K / 2-4																									
ASW#15 - Missing Dowels																									
Str Stl Columns Set 1st Tier Area 2																									
Str Stl Columns Set 1st Tier Area 1																									
High Strength Grout to Str Stl. Base Plates																									
ASW #7 Stl Columns Not Plumb																									
Column Ftg Incomplete Track Area 2 (3 cols.)																									
Slab on Grade, N. Side of Foundation																									
Erected 1st Tier Building Columns																									
East / West Connector (Procurement)																									
Interference of Tie Backs - C2 Level																									
E/W Connector: Design Interface w/ Mem.																									
Northeast Crashwall Tray Impact																									
Footing #7 Column																									
Str. Column Steel Late For J Line & 7 Line																									
E / W Connector Westside 8-line Column																									
Area 4 -Erect 2nd Tier Str. Steel Columns																									
Area 3 -Erect 2nd Tier Str.Stl Col. + T&P																									
Area 2 -Erect 2nd Tier Str.Stl Col. + T&P																									
Area 1 -Erect 2nd Tier Str.Stl Col. + T&P																									
Delay Area 1 - Footings Not Complete At C2 Level																									
Tank Walls Area 2 Fdn to B4M -Missing Dowls																									
Col. Area 4 to be Re-located (13.4/D)																									
Ftg.#8 -Added Str.Columns (Bul.#12)(Rebar)																									
Col. C.5 - Foundation Not Complete																									
Grid 7 - A Frame Str Steel Work																									
Grid D/3- Col. Ftg. Incomplete- Ex.C5 to C4 Lev																									
E. Crash Wall Ftg. Dowls Grid K/15.2 (Area 4)																									
B/4 Col. Ftg Missing Ex.C5 to Ex.C4 (Area 1)																									
Ftg. D.4/2.4 - Miss Aligned (Area 3)																									
RFI 137 - Col. J.2/10 Inter. w/ Cross Bracing																									
Col. C/3.7 Key Detail to Ex. D4 Slab																									
Ftg.#8 Rework of Stl Plates (TCC RFI749)																									
Col C/7 Str Steel not Plumb&True for Grout																									
Ftg#8 Redesign to Shoring&Geometry of Col																									
Col C.4/12 - Change to Design																									
Sub - Contractor Not on Site																									
N/W Corner(RFI #127) Couplers@ Cols&Walls/Access																									
Col. D/3.4 (Ftg #7) - Added Key Detail																									
Str Steel Columns Not Installed (Area 4)																									
Column Reinforcing rework (C.1/10, C4MtoC3)																									
Limited Access to C5 Level																									
Changes to Col. Rebar lineB.4/12 Lev B4M-B3 A2																									
Asbestos Abatement N/W Corner A5 Level																									
Col D/3- Shut Down Coordination																									
SSK 135 Required resubmittal of 7-line Shop Dwgs																									
Col E/3 C3-C2 - Added M & E Sleeves																									
Use of Weldable Couplers in 7-line Beam																									
7-Line Windscreen and Cable Net Anchors- Area 4																									
7-Line Windscreen and Cable Net Anchors- Area 3																									
Change Epoxy Rebar Requirements for 7-line Beam																									
ASW6- Revised Bar Details w/ Str. Steel																									
South Tower Crane Out of Service																									
7-Line Added Stirrups																									
ASW#5 - Existing Rebar Conditions																									
Incomplete Str. Steel at 7-Line Columns - Area 3																									

SUPPLEMENTARY WORK

WALLS & COLUMNS

WALLS & COLUMNS SUMMARY - FND -C6
WALLS & COLUMNS SUMMARY - C6-C5
WALLS & COLUMNS SUMMARY - C5-C4
WALLS & COLUMNS SUMMARY - C3-C2
WALLS & COLUMNS SUMMARY - C1-Ground

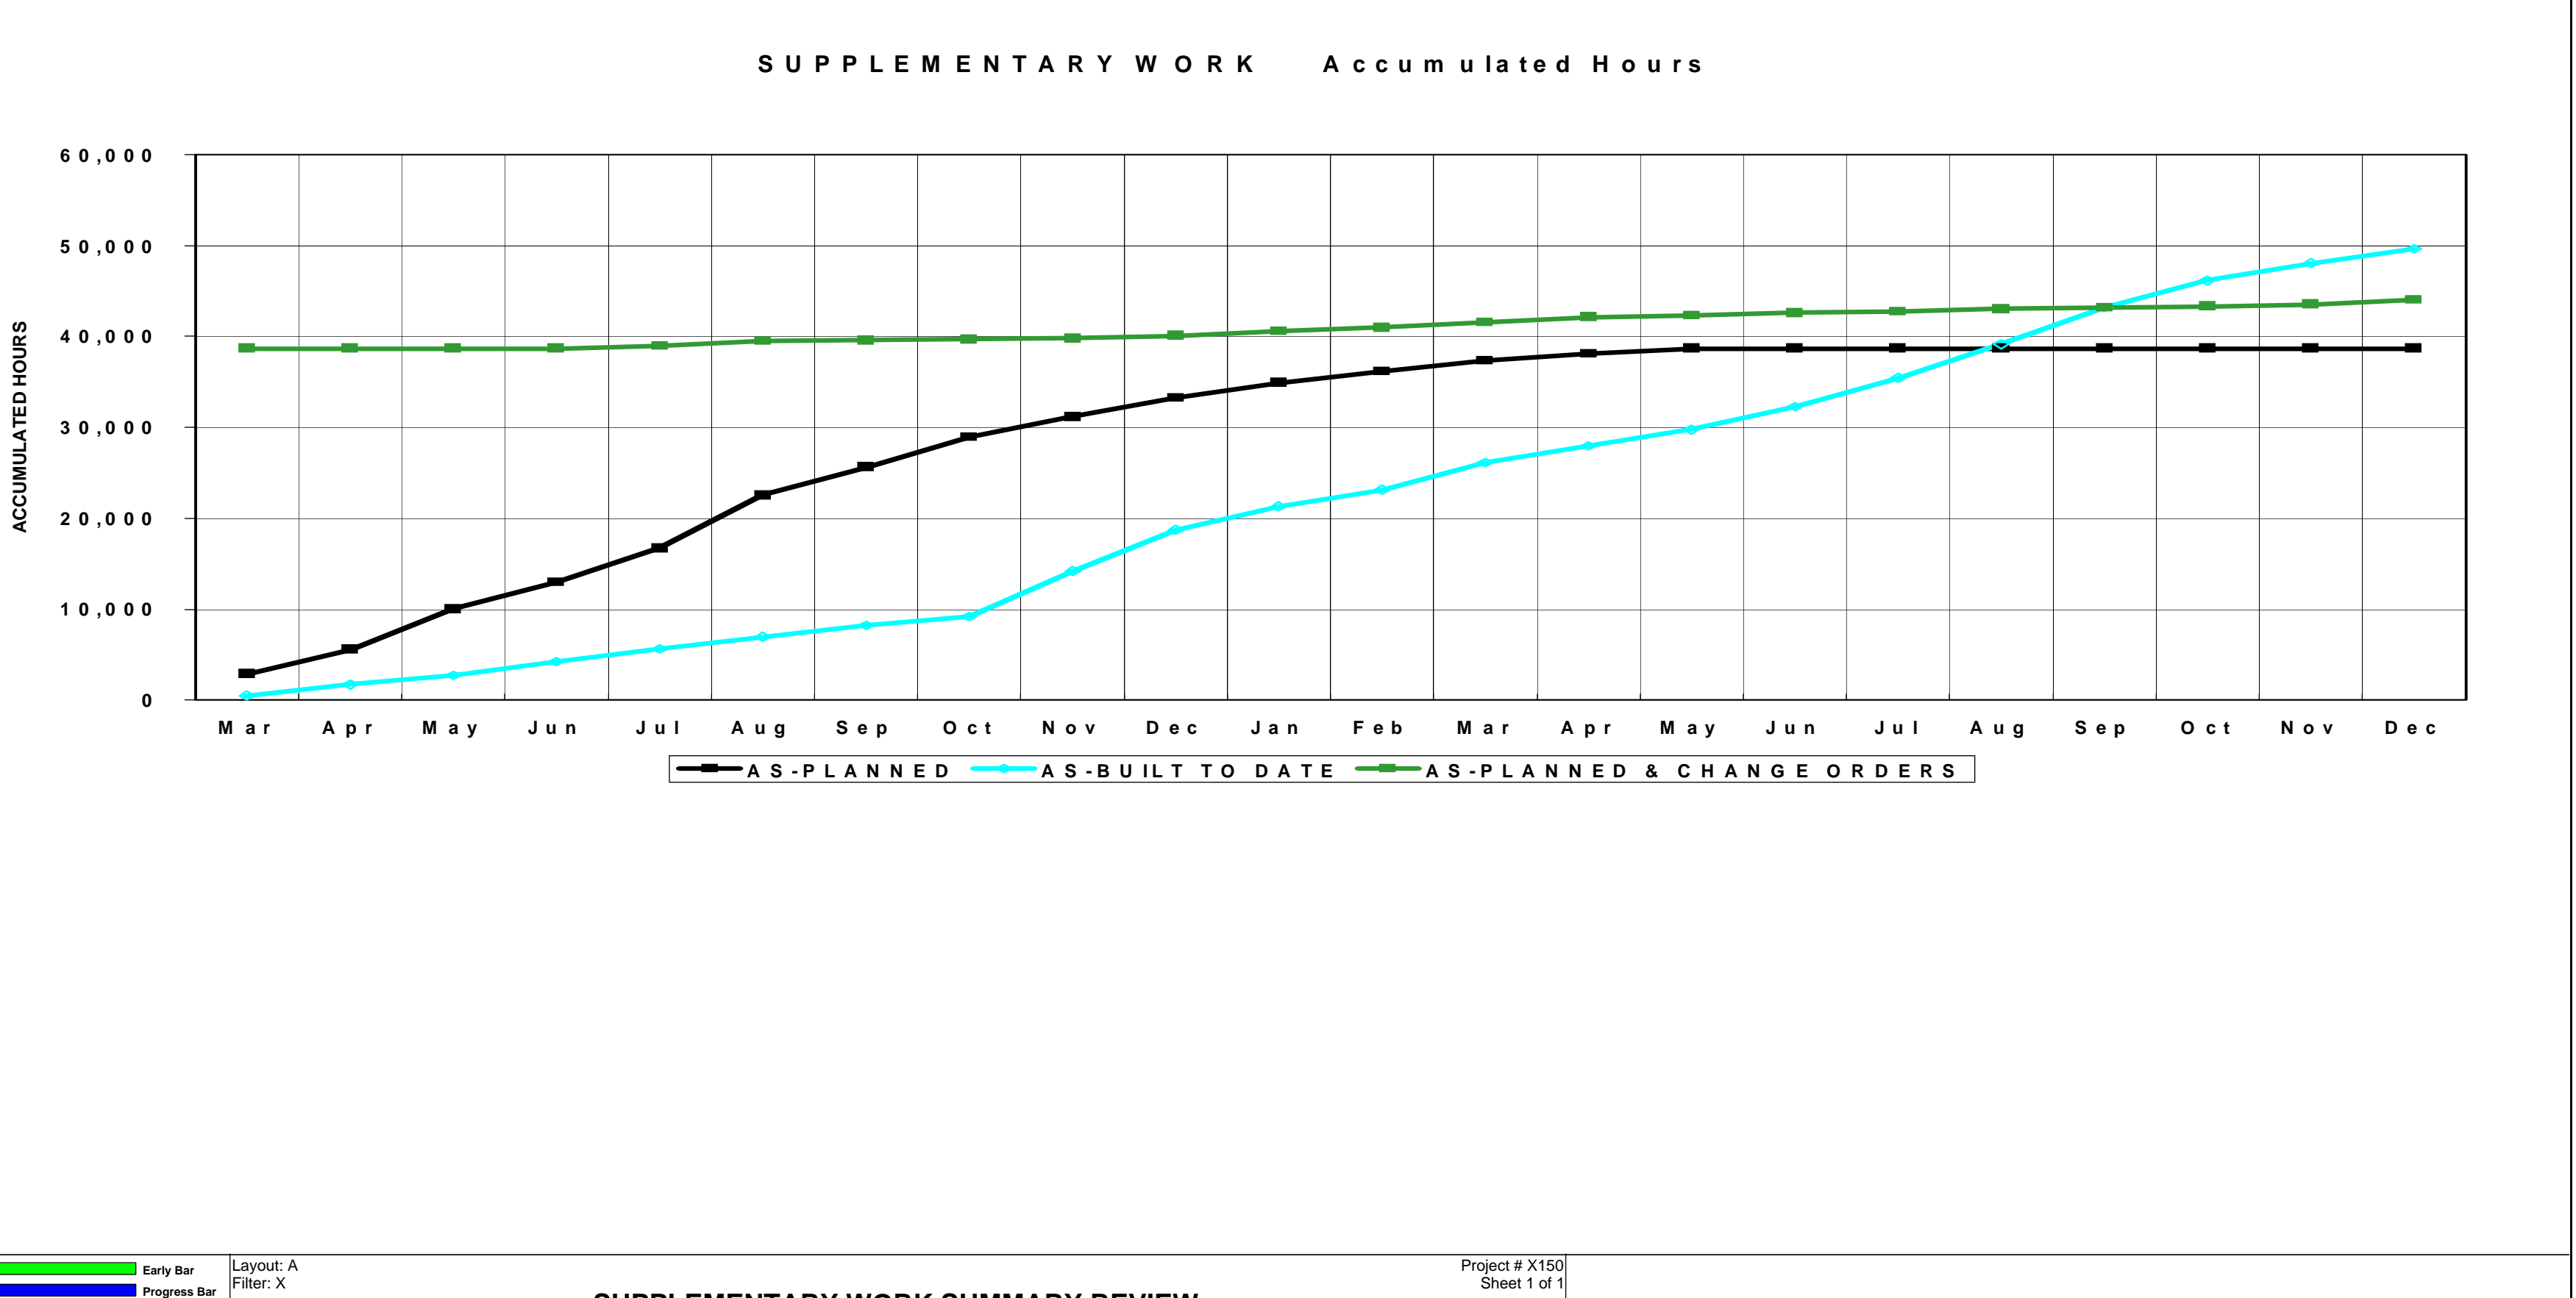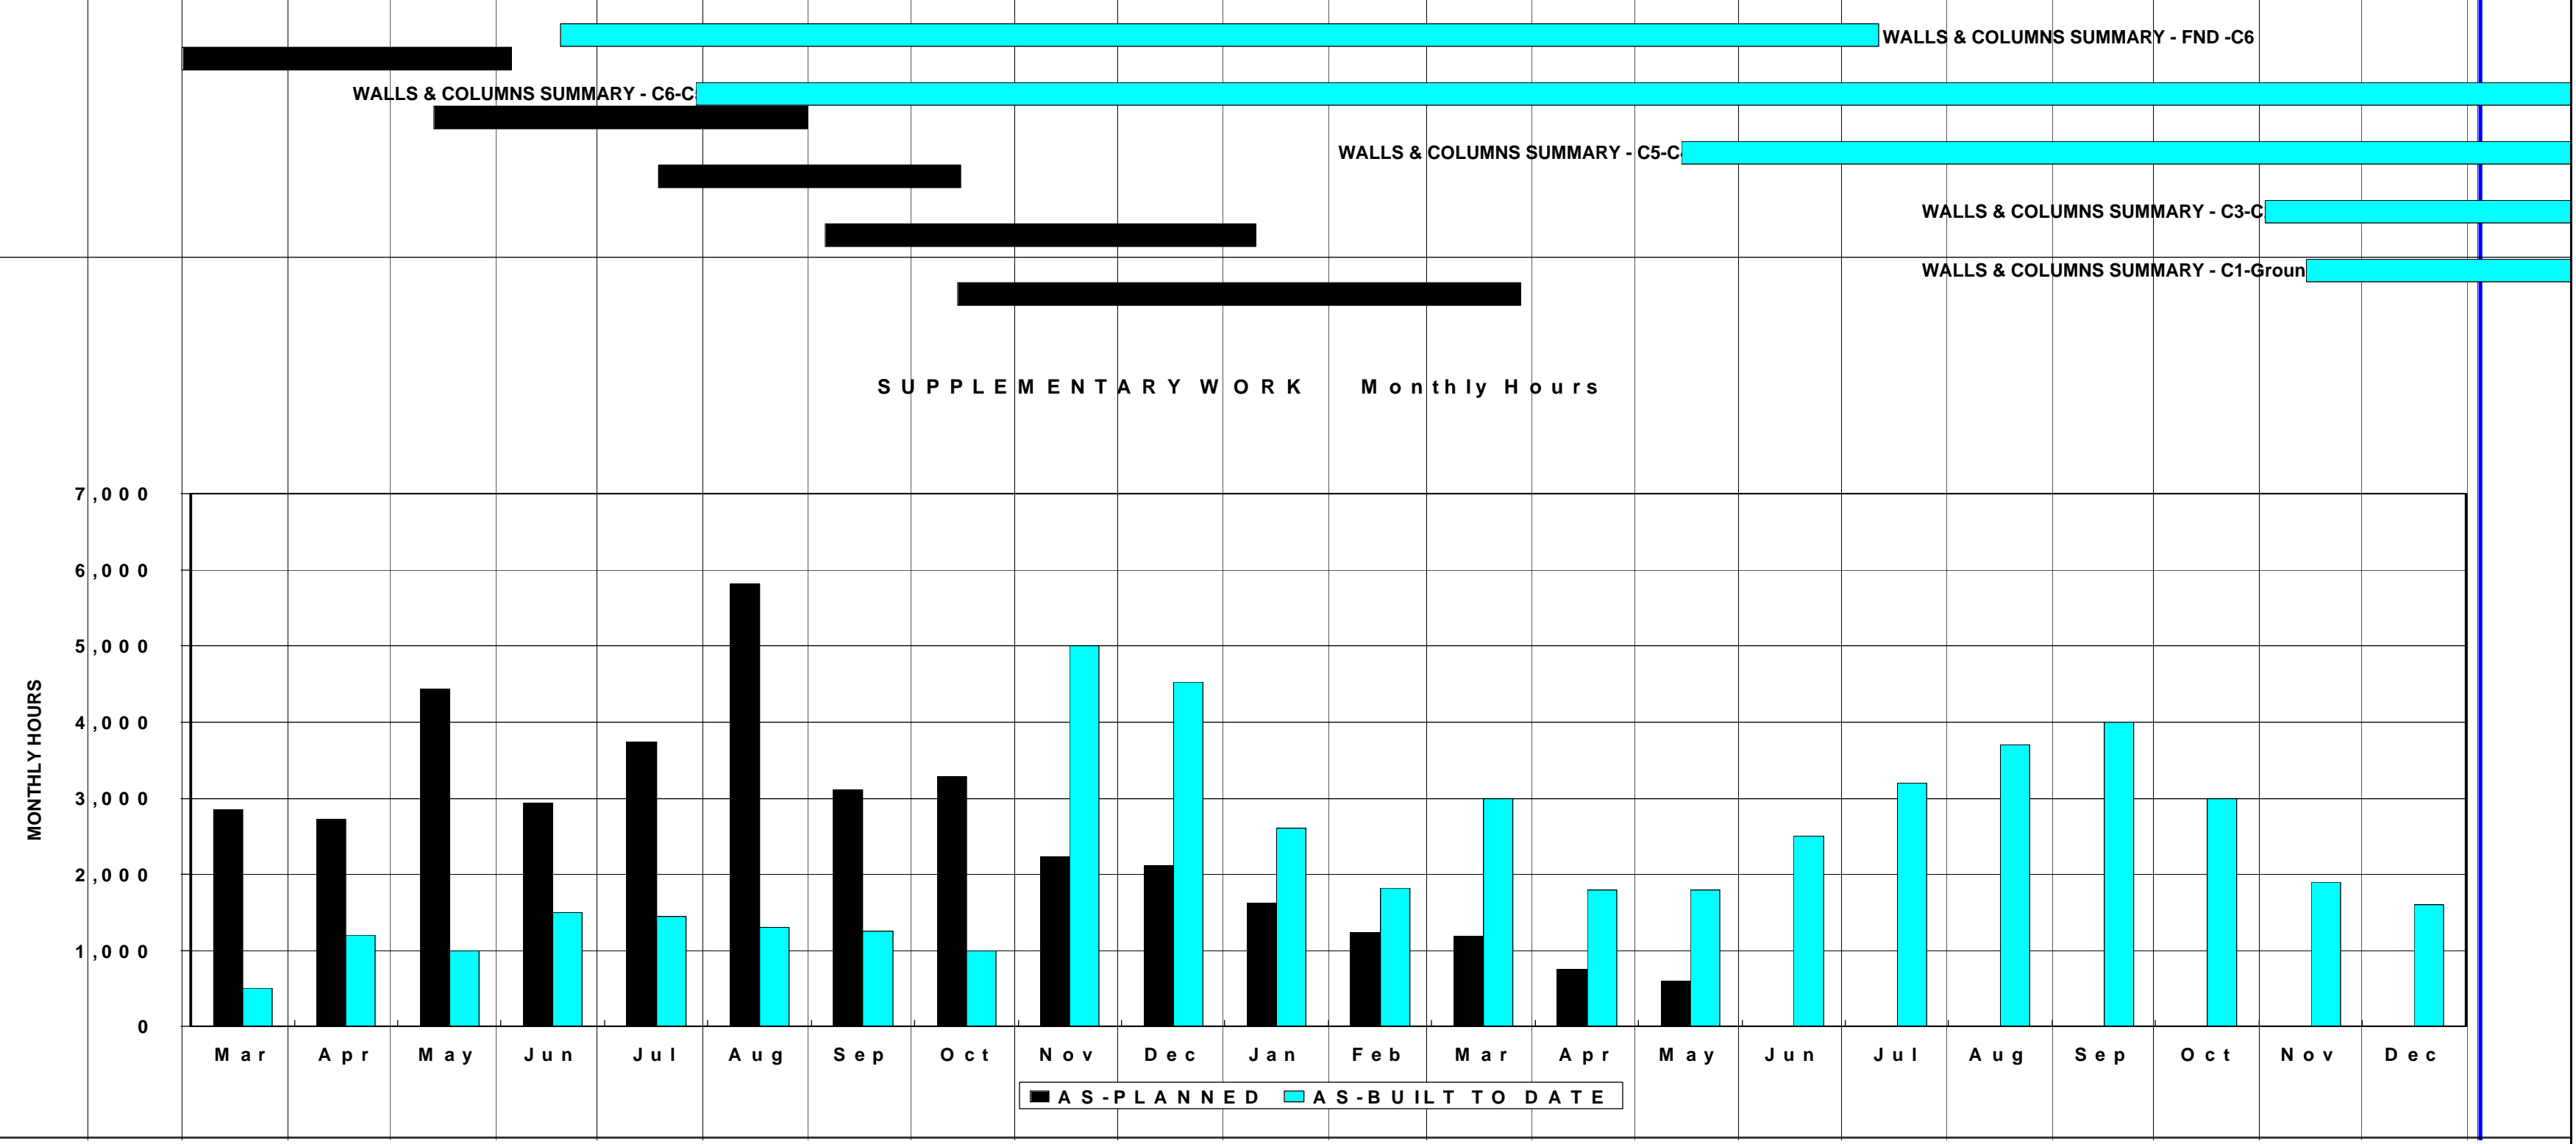

Legend:
█ Early Bar
█ Progress Bar
█ Critical Activity

Layout: A
Filter: X
